Home Inspection Services



3107 Snug Harbor Ct Katy, TX 77449



PROPERTY INSPECTION REPORT FORM

| Jordan Briones | 08/07/2022 |
|--|--------------------|
| Name of Client | Date of Inspection |
| 3107 Snug Harbor Ct, Katy, TX 77449 Address of Inspected Property | |
| Mark McCullough | 9139 |
| Name of Inspector | TREC License # |
| Name of Sponsor (if applicable) | TREC License # |

PURPOSE OF INSPECTION

A real estate inspection is a visual survey of a structure and a basic performance evaluation of the systems and components of a building. It provides information regarding the general condition of a residence at the time the inspection was conducted. *It is important* that you carefully read ALL of this information. Ask the inspector to clarify any items or comments that are unclear.

RESPONSIBILITY OF THE INSPECTOR

This inspection is governed by the Texas Real Estate Commission (TREC) Standards of Practice (SOPs), which dictates the minimum requirements for a real estate inspection.

The inspector IS required to:

- use this Property Inspection Report form for the inspection;
- inspect only those components and conditions that are present, visible, and accessible at the time of the inspection;
- indicate whether each item was inspected, not inspected, or not present;
- indicate an item as Deficient (D) if a condition exists that adversely and materially affects the performance of a system or component **OR** constitutes a hazard to life, limb or property as specified by the SOPs; and
- explain the inspector's findings in the corresponding section in the body of the report form.

The inspector IS NOT required to:

- identify all potential hazards;
- turn on decommissioned equipment, systems, utilities, or apply an open flame or light a pilot to operate any appliance;
- climb over obstacles, move furnishings or stored items;
- prioritize or emphasize the importance of one deficiency over another;
- provide follow-up services to verify that proper repairs have been made; or
- inspect system or component listed under the optional section of the SOPs (22 TAC 535.233).

RESPONSIBILITY OF THE CLIENT

While items identified as Deficient (D) in an inspection report DO NOT obligate any party to make repairs or take other actions, in the event that any further evaluations are needed, it is the responsibility of the client to obtain further evaluations and/or cost estimates from qualified service professionals regarding any items reported as Deficient (D). It is recommended that any further evaluations and/or cost estimates take place prior to the expiration of any contractual time limitations, such as option periods.

Please Note: Evaluations performed by service professionals in response to items reported as Deficient (D) on the report may lead to the discovery of additional deficiencies that were not present, visible, or accessible at the time of the inspection. Any repairs made after the date of the inspection may render information contained in this report obsolete or invalid.

REPORT LIMITATIONS

This report is provided for the benefit of the named client and is based on observations made by the named inspector on the date the inspection was performed (indicated above).

ONLY those items specifically noted as being inspected on the report were inspected.

This inspection IS NOT:

- a technically exhaustive inspection of the structure, its systems, or its components and may not reveal all deficiencies;
- an inspection to verify compliance with any building codes;
- an inspection to verify compliance with manufacturer's installation instructions for any system or component and DOES NOT imply insurability or warrantability of the structure or its components.

NOTICE CONCERNING HAZARDOUS CONDITIONS, DEFICIENCIES, AND CONTRACTUAL AGREEMENTS

Conditions may be present in your home that did not violate building codes or common practices in effect when the home was constructed but are considered hazardous by today's standards. Such conditions that were part of the home prior to the adoption of any current codes prohibiting them may not be required to be updated to meet current code requirements. However, if it can be reasonably determined that they are present at the time of the inspection, the potential for injury or property loss from these conditions is significant enough to require inspectors to report them as Deficient (D). Examples of such hazardous conditions include:

- malfunctioning, improperly installed or missing ground fault circuit protection (GFCI) devices and arc-fault devices;
- ordinary glass in locations where modern construction techniques call for safety glass;
- malfunctioning or lack of fire safety features such as, smoke alarms, fire-rated doors in certain locations, and functional emergency escape and rescue openings in bedrooms;
- malfunctioning carbon monoxide alarms;
- excessive spacing between balusters on stairways and porches;
- improperly installed appliances;
- improperly installed or defective safety devices;
- lack of electrical bonding and grounding; and
- lack of bonding on gas piping, including corrugated stainless steel tubing (CSST).

Please Note: items identified as Deficient (D) in an inspection report DO NOT obligate any party to make repairs or take other actions. The decision to correct a hazard or any deficiency identified in an inspection report is left up to the parties to the contract for the sale or purchase of the home.

This property inspection report may include an inspection agreement (contract), addenda, and other information related to property conditions.

INFORMATION INCLUDED UNDER "ADDITIONAL INFORMATION PROVIDED BY INSPECTOR", OR PROVIDED AS AN ATTACHMENT WITH THE STANDARD FORM, IS NOT REQUIRED BY THE COMMISSION AND MAY CONTAIN CONTRACTUAL TERMS BETWEEN THE INSPECTOR AND YOU, AS THE CLIENT. THE COMMISSION DOES NOT REGULATE CONTRACTUAL TERMS BETWEEN PARTIES. IF YOU DO NOT UNDERSTAND THE EFFECT OF ANY CONTRACTUAL TERM CONTAINED IN THIS SECTION OR ANY ATTACHMENTS, CONSULT AN ATTORNEY.

| | ADD | ITIONA | L INFORMA | TION PROVIDED BY | INSPECTOR |
|--|----------|----------|-----------------------------------|----------------------------|---------------------|
| Present at Inspection: | 🛛 Buyer | 🗆 Sellir | ng Agent | Listing Agent | Occupant |
| Building Status: | 🗹 Vacant | 🗌 Own | er Occupied | Tenant Occupied | Other |
| Weather Conditions: | 🗹 Fair | 🗌 Clou | dy | 🗆 Rain | Temp: |
| Utilities On: | 🗹 Yes | 🗆 No V | Vater | No Electricity | 🗆 No Gas |
| Special Notes: | | | | | |
| | | INAC | CESSIBLE | OR OBSTRUCTED AR | EAS |
| ☑ Sub Flooring | | | Attic Space | e is Limited - Viewed fro | m Accessible Areas |
| ✓ Floors Covered | | | Plumbing | Areas - Only Visible Plur | nbing Inspected |
| Walls/Ceilings Covered or Freshly Painted | | | Siding Over Older Existing Siding | | |
| Behind/Under Furniture and/or Stored Items | | | Crawl Spa | ice is limited - Viewed Fr | om Accessible Areas |

Mold/Mildew investigations are NOT included with this report; it is beyond the scope of this inspection at the present time. Any reference of water intrusion is recommended that a professional investigation be obtained.

NOTICE: THIS REPORT IS PAID FOR BY AND PREPARED FOR THE CLIENT NAMED ABOVE. THIS REPORT IS NOT VALID WITHOUT THE SIGNED SERVICE AGREEMENT AND IS NOT TRANSFERABLE.

 $\overline{\mathbf{A}} \square \square \overline{\mathbf{A}}$

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient | |
|-------------|------------------|------------------|--------------------|--|
| I NI NP D | | | | |
| | | I. STRUCTURAL SY | STEMS | |

I. STRUCTURAL SY

A. Foundations
 Type of Foundation(s): Post Tension
 Comments:
 Signs of Structural Movement or Settling





Strike plate / alignment at pantry door and back bedroom



Floors not level and or debris under carpet in primary bedroom





 \blacksquare Separations between trim and siding

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient |
|-------------|------------------|----------------|-------------|
| I NI NP D | | | |



Missed brick ledge at time of construction at entry



Corner cracks on foundation due to thermal expansion of bricks (cosmetic)

Performance Opinion: (An opinion on performance is mandatory)

Note: Weather conditions, drainage, leakage and other adverse factors are able to effect structures, and differential movements are likely to occur. The inspectors opinion is based on visual observations of accessible and unobstructed areas of the structure at the time of the inspection. Future performance of the structure cannot be predicted or warranted.

Some movement and or settling noted; however, the foundation is supporting the structure at this time.

SUGGESTED FOUNDATION MAINTENANCE & CARE - Proper drainage and moisture maintenance to all types of foundations due to the expansive nature of the area load bearing soils. Drainage must be directed away from all sides of the foundation with grade slopes. In most cases, floor coverings and/or stored articles prevent recognition of signs of settlement - cracking in all but the most severe cases. It is important to note, this was not a structural engineering survey nor was any specialized testing done of any sub-slab plumbing systems during this limited visual inspection, as these are specialized processes requiring excavation. In the event that structural movement is noted, client is advised to consult with a Structural Engineer who can isolate and identify causes, and determine what corrective steps, if any, should be considered to either correct and/or stop structural movement.

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient | |
|-------------|------------------|----------------|-------------|--|
| I NI NP D | | | | |
| | | | | |

 $\boxdot \Box \Box \blacksquare$

B. Grading and Drainage

Comments:

Note: Any area where the ground or grade does not slope away from the structure is to be considered an area of improper drainage. Six inches per 10 feet.





Improper drainage from foundationErosion or ponding next to foundation






Level lot, does not facilitate proper drainage

 $\boxdot \Box \Box \checkmark$

C. Roof Covering Materials

Type(s) of Roof Covering: Composition Asphalt Shingles *Viewed From*: Drone *Comments*:

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient | |
|-------------|------------------|----------------|--------------------|--|
| I NI NP D | | | | |
| | | | | |







Weathered shingles



 ${\ensuremath{\overline{\!\!\mathcal M\!}}}$ Brick chimney not properly flashed and or lifted flashing

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient |
|-------------|------------------|----------------|-------------|
| I NI NP D | | | |



Gutters need cleaning



☑ Flashing is lifting, ill configured



| I NI NP D | I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient | |
|-----------|-------------|------------------|----------------|--------------------|--|
| | I NI NP D | | | | |





Roof penetration(s) not properly caulked / sealed



☑ Improper clearance between roof and siding

 $\boxdot \Box \Box \checkmark$

D. Roof Structures and Attics

Viewed From: Some areas Obstructed from view *Approximate Average Depth of Insulation*:4-8 *Approximate Average Thickness of Vertical Insulation*:0-6 *Comments*:



| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient |
|-------------|------------------|----------------|-------------|
| I NI NP D | | | |

☑ Water stained, damaged decking






Evidence of rodents in attic



 \blacksquare Evidence of insulation voids and poor installation


| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient |
|-------------|------------------|----------------|-------------|
| I NI NP D | | | |
| | | | |



 ${\ensuremath{\overline{\!\!\mathcal M\!}}}$ Recommend door locks be installed at walk in attic access doors

- $\boxdot \Box \Box \blacksquare$
- E. Walls (Interior and Exterior) Comments:



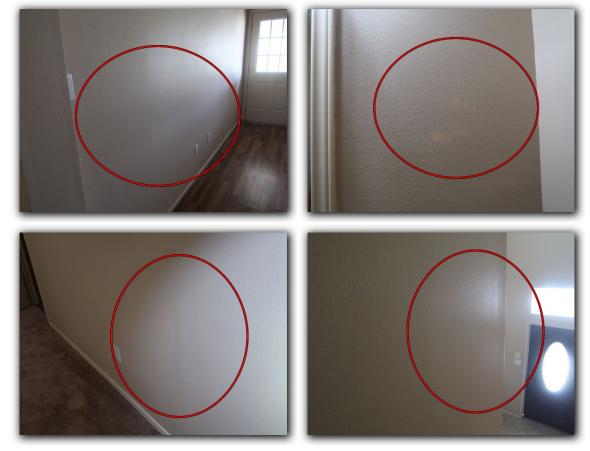

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient | |
|-------------|------------------|----------------|-------------|--|
| I NI NP D | | | | |
| | | | | |



☑ Visible tape joints, patches, stains, poor finish in some areas

Exterior Walls:



| I=Inspected I NI NP D | NI=Not Inspected | NP=Not Present | D=Deficient | |
|--------------------------|------------------|----------------|-------------|---|
| | | | | 5 |
| | | | | |



| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient | |
|-------------|------------------|----------------|--------------------|--|
| I NI NP D | | | | |
| | | | | |



 ${\ensuremath{\overline{\!\!\mathcal M\!}}}$ Damaged, separated, stained, poor finish cement board siding and trim boards



Mortar is separated or missing in some areas

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient | |
|-------------|------------------|----------------|-------------|--|
| I NI NP D | | | | |
| | | | | |





Caulking / sealant is separated or missing in some areas



Dirty, stained bricks



Previous brick / mortar repairs at garage



F. Ceilings and Floors

Comments:

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient | |
|-------------|------------------|----------------|--------------------|--|
| I NI NP D | | | | |
| | | | | |



| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient | |
|-------------|------------------|----------------|-------------|--|
| I NI NP D | | | | |
| | | | | |



 \blacksquare Ceiling cracks, tape joints, nail pops, patches, stains and or poor finish in some areas



| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient | |
|-------------|------------------|----------------|--------------------|--|
| I NI NP D | | | | |
| | | | | |



| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient | |
|-------------|------------------|----------------|--------------------|--|
| I NI NP D | | | | |
| | | | | |



 \blacksquare Cracked, loose, poor installation tile and missing grout kitchen, entry and bathrooms



Damaged, separated flooring

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient |
|-------------|------------------|----------------|-------------|
| I NI NP D | | | |



☑ Loose, warped trim board



Dirty, stained, poor installation carpet back bedroom



| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient |
|-------------|------------------|----------------|-------------|
| I NI NP D | | | |



☑ Loose / Unlevel floor decking upstairs (Common on two story houses new and old)

 $\boxdot \Box \Box \blacksquare$

G. Doors (Interior and Exterior) Comments:
Interior Doors
☑ Performing as intended at time of inspection

Exterior Doors



Damaged, missing weather strip at front door

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient |
|-------------|------------------|----------------|-------------|
| I NI NP D | | | |
| | | | |

Garage Doors





Doors / panels are bent

$\boxdot \Box \Box \boxdot$

H. Windows Comments:





Clean and seal rusted / exposed lintels above some windows



 \blacksquare Some windows are difficult to open or close living room and primary bathroom

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient | |
|-------------|------------------|----------------|--------------------|--|
| I NI NP D | | | | |







 \blacksquare Some window lift supports are loose, damaged or missing living room, upstairs back bedrooms



 \blacksquare Some window screens are damaged or missing

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient |
|-------------|------------------|----------------|-------------|
| I NI NP D | | | |



☑ Inspection of some windows was limited



Caulking / plastic , etc. damaged and or missing

 $\boxdot \Box \Box \Box$

I. Stairways (Interior and Exterior) Comments: INTERIOR

 $\boxdot \Box \Box \Box$

J. Fireplaces and Chimneys Comments: Type of Fireplace: ☑ Factory

□ Masonry

□ Free Standing

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient |
|-------------|------------------|----------------|-------------|
| I NI NP D | | | |




Dirty, stained, previous tile grout repair



K. Porches, Balconies, Decks, and Carports *Comments*:





Cracks in driveway and back patio



Some settlement at sidewalk

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient |
|-------------|------------------|----------------|-------------|
| I NI NP D | | | |



☑ Damaged support at back patio column



☑ Small hole in ceiling at back patio



 ${\ensuremath{\overline{\!\!\mathcal M\!}}}$ Missing siding, trim, flashing at back patio cover

 $\boxdot \Box \Box \boxtimes$

L. Other

Comments:

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient | |
|-------------|------------------|----------------|--------------------|--|
| I NI NP D | | | | |



Damaged fence pickets and gate needs adjustment


II. ELECTRICAL SYSTEMS



A. Service Entrance and Panels *Comments*:

□ Overhead Service ☑ Underground Service

Main Disconnect Panel 100 amp



☑ Label one breaker



| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient | |
|-------------|------------------|----------------|-------------|--|
| I NI NP D | | | | |
| | | | | |

Missing caulking around meter

☑ □ □ ☑ B. Branch Circuits, Connected Devices, and Fixtures

Type of Wiring: \square Copper \square Aluminum Conduit *Comments*:

Outlet and Switches



Missing weatherproof cover at back patio



Missing and or removed outlet below kitchen countertop

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient |
|-------------|------------------|----------------|-------------|
| I NI NP D | | | |



 \blacksquare One or more junction boxes do not have covers



GFCI is inoperable at back patio

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient | |
|-------------|------------------|----------------|--------------------|--|
| I NI NP D | | | | |

Ground Fault Circuit Interrupt Safety Protection







☑ No GFCI protection at one or more location. This is considered a recognized safety hazard.

Fixtures



Ceiling fan is loose, noisy, unlevel in primary bedroom

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient |
|-------------|------------------|----------------|-------------|
| I NI NP D | | | |



☑ Loose, warped fan blades at back patio

Smoke and Fire Alarms

C. Other Comments:

III. HEATING, VENTILATION AND AIR CONDITIONING SYSTEMS



A. Heating Equipment Type of System: Central Energy Source: Gas Comments:



☑ Blower fan assembly is vibrating
 ☑ Recommend cleaning, servicing, and further evaluation by a licensed professional



B. Cooling Equipment *Type of System*: Central

Comments:

🗹 Unit #1: 2013 4 TON

☑ Temperature differential is not within range of 14-23 degrees Fahrenheit

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient | |
|-------------|------------------|----------------|-------------|--|
| I NI NP D | | | | |



Noisy compressor



Evaporator coil is not properly sealed




☑ Rust and corrosion in drain pan

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient |
|-------------|------------------|----------------|-------------|
| I NI NP D | | | |



☑ Improper condensation drain line termination
 ☑ Recommend cleaning, servicing and or further evaluation by a licensed professional

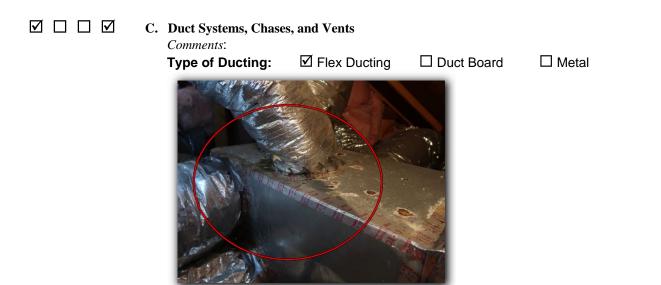

Evidence of excessive condensation / bio-growth on ducts and or plenum



| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient |
|-------------|------------------|----------------|-------------|
| I NI NP D | | | |



☑ Some torn ducts



☑ Inadequate support of duct work



Return air filter needs replacement

D. Other *Comments*:

REI 7-6 (8/9/21)

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient |
|-------------|--|---|--|
| I NI NP D | | | |
| | | IV. PLUMBING SYS | STEMS |
| | A. Plumbing Supply, Dist Location of water meter Location of main water Static water pressure re Type of supply piping m Comments: Water Source: ☑ Po Sinks Comments: | supply valve: Garage ading: 50 aterial: PVC | es Г уре: ☑ Public □ Private |



☑ Water stained, damaged, poor finish cabinet bottoms

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient |
|-------------|------------------|----------------|-------------|
| I NI NP D | | | |



☑ Clean and or replace aerator at half bathroom



☑ Some cabinet doors need adjustment



 \blacksquare Missing caulking and or poor installation sink faucet hall bathroom

Bathtubs and Showers Comments: _____

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient |
|-------------|------------------|----------------|-------------|
| I NI NP D | | | |



 \blacksquare Dirty, stained, poor finish shower pan at primary bathroom




☑ Caulking or grout missing or damaged at primary bathroom

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient |
|-------------|------------------|----------------|-------------|
| I NI NP D | | | |



 \blacksquare Shower diverter value not operating properly at hall bathroom

Commodes Comments:



Rebuild toilets at half bathroom and primary bathroom



☑ Loose toilet tank at half bathroom

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient |
|-------------|------------------|----------------|-------------|
| I NI NP D | | | |



☑ Loose flush handle at hall bathroom

Exterior Plumbing Comments:



Exterior hose bibs do not have back-flow prevention

B. Drains, Wastes, and Vents
Type of drain piping material: PVC
Comments:
☑ Performing as intended at time of inspection

C. Water Heating Equipment

Energy Source: Gas Capacity: 40 gallon Comments:

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient | |
|-------------|------------------|----------------|-------------|--|
| I NI NP D | | | | |
| | | | | |



Cloudy water at some fixtures recommend water heater be flushed



☑ Vent pipe needs adjustment and missing strap

| | V | V | | |
|-------------------|---|---|--------------|--|
| $\mathbf{\nabla}$ | | | \checkmark | |

- **D. Hydro-Massage Therapy Equipment** *Comments*:
- ✓ E. Gas Distribution Systems and Gas Appliances Location of gas meter: Right side of House Type of gas distribution piping material: Steel

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient |
|-------------|------------------|----------------|-------------|
| I NI NP D | | | |
| | | | |

Comments:



Some surface rust on gas line (clean and seal)

F. Other Comments:

V. APPLIANCES

A. Dishwashers Comments:



 \blacksquare No anti-siphon loop at the drain line

B. Food Waste Disposers Comments:

 ${\ensuremath{\overline{\mathrm{v}}}}$ Performing as intended at time of inspection

 $\overline{\square} \square \square \overline{\square}$

C. Range Hood and Exhaust Systems *Comments*:

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient | |
|-------------|------------------|----------------|-------------|--|
| I NI NP D | | | | |



Missing one filter

 ☑ □ □ □ □
 D. Ranges, Cooktops, and Ovens Comments:
 Range Type: □ Electric ☑ Gas
 ☑ Performing as intended at time of inspection

| \checkmark | | |
|--------------|--|--|
| | | |

E. Microwave Ovens

Comments: ☑ Performing as intended at time of inspection


 $\overline{\mathbf{A}} \square \square \overline{\mathbf{A}}$

F. Mechanical Exhaust Vents and Bathroom Heaters Comments:



 \blacksquare Unit motor and or fan is noisy hall bathroom

| I=Inspected | NI=Not Inspected | NP=Not Present | D=Deficient | |
|-------------|---------------------------------------|-----------------------------------|--------------------|--|
| I NI NP D | | | | |
| | G. Garage Door Operators Comments: | s nected at time of inspection | n (Consult Owner) | |



H. Dryer Exhaust Systems Comments:

I. Other Comments:
