



COASTAL TESTING LABORATORIES, INC.

1217/1221 GEORGIA AVE. • 713-477-0121 • FAX 713-477-2277 • P.O. BOX 148 • DEER PARK, TEXAS 77536

DAILY ACTIVITY REPORT

Project Number 22-618 Service Date 7/25/2022 Page 1
Project Name Residence 2625 Broadway - Port Bolivar Report Number 220725-24187
Contractor Craig McClelland Report Date 7/26/2022
Bill To Craig McClelland Contract No PO No COD
Job No File No GFS No
Supplier

On July 25, 2022, a Coastal Testing representative was present at the above referenced project, as scheduled to obtain a soil sample at 2625 Broadway. The technician obtained one (1) natural ground sample and transported the soil sample to the laboratory to be stored, cured, and tested.

Charges: 3 1/2 Hours Technician + 1 Standard Proctor + 1 Pi + 1 Vehicle Charge

Typed by: RR


Technician Erik Garza	Test Date 7/25/2022
Lab Departure Time 8:30 AM	Project Arrival Time 10:00 AM
Lab Return Time 12:00 PM	Project Departure Time 10:30 AM
Standby Time	Lunch N/A
Straight Hours 3 1/2 Hours	Overtime Hours

Note: If applicable, concrete tests will come separately.

Respectfully Submitted:


Coastal Testing Laboratories, Inc.

PROCTOR TEST REPORT

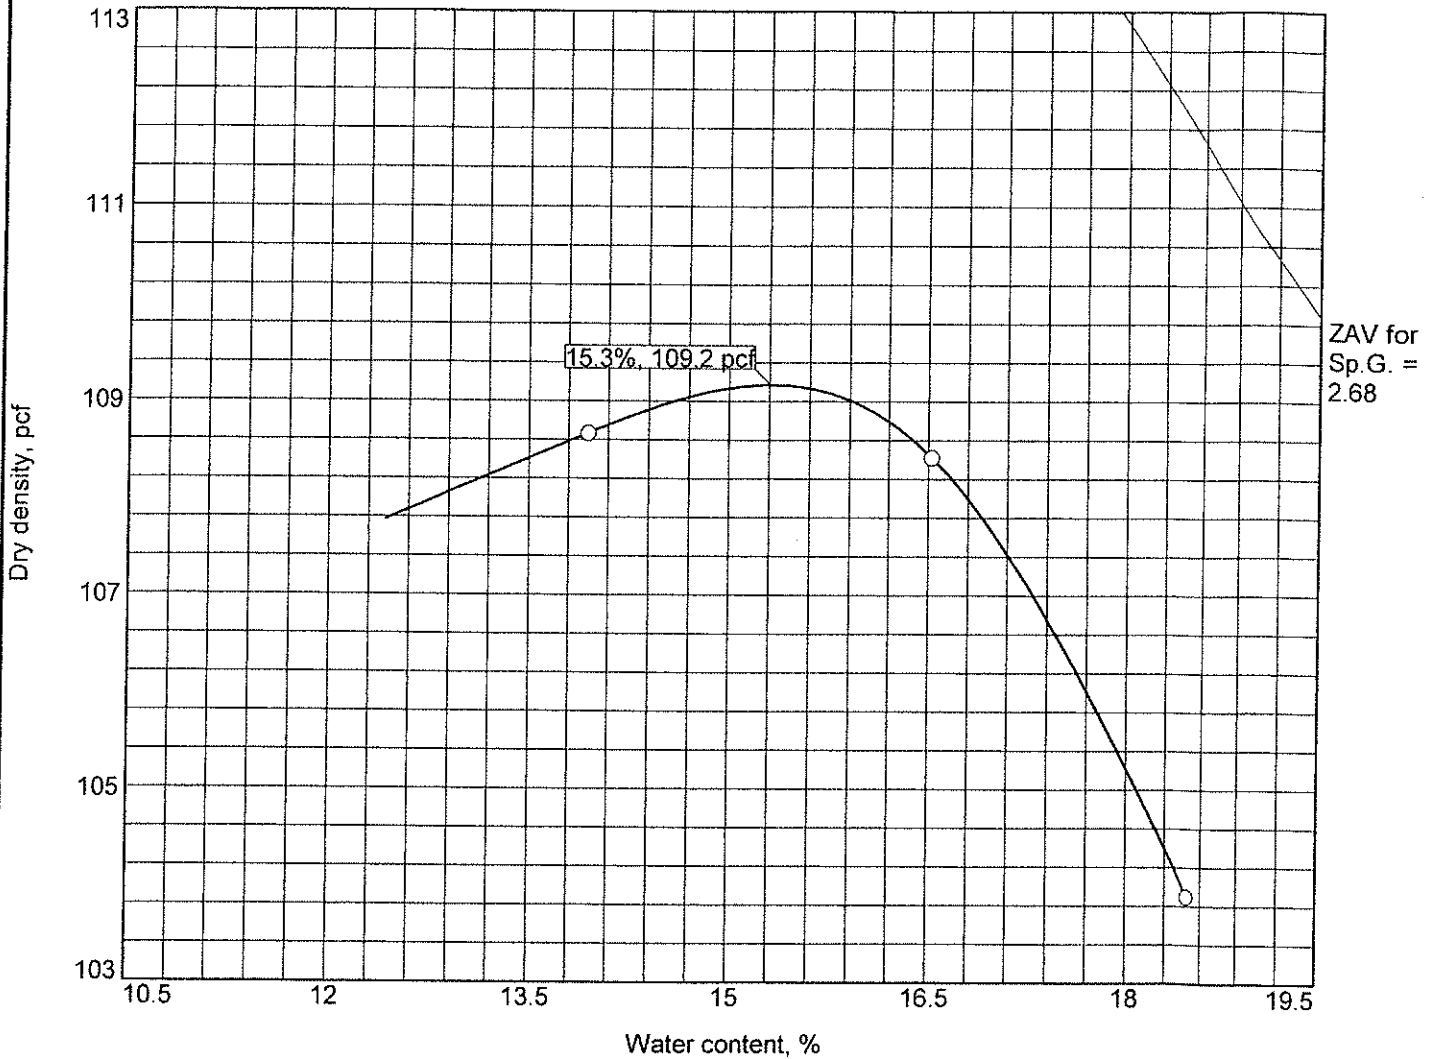

Test specification: ASTM D 698-12 Method A Dry, ASTM D 4318-17, ASTM D 1140 Method B Standard

Elev/ Depth	Classification		Nat. Moist.	Sp.G.	LL	PI	% > #4	% < No.200
	USCS	AASHTO						
	SP -Poorly Graded Sand		12.7		24	3		23.2

TEST RESULTS	MATERIAL DESCRIPTION
Maximum dry density = 109.2 pcf Optimum moisture = 15.3 %	Brown Sandy Clay

Project No. 22-618 Client: Craig McClelland Project: McClelland Residence 2625 Broadway Port Bolivar, Texas ○ Source of Sample: Excavated Material Sample Number: S-15056 Coastal Testing Laboratories, Inc. <p style="text-align: center;">Pasadena, TX</p>	Remarks: Report Date: 7/27/2022 Rpt No: 220725-24187 Sample Date: 7/25/2022 By: Eric Garza Charges: 1 Std Proctor, 1 Pi, See Daily Report End of Proctor Report
--	--

The above tests results relate only to items actually tested. This report shall not be reproduced except in full without the approval of this laboratory.

Tested By: Evan Spivey 7/26/2022 **Checked By:** Joe A Gallardo 7/27/2022



COASTAL TESTING LABORATORIES, INC.

1217/1221 GEORGIA AVE. • 713-477-0121 • FAX 713-477-2277 • P.O. BOX 148 • DEER PARK, TEXAS 77536

DAILY ACTIVITY REPORT

Project Number	22-618	Service Date	8/1/2022	Page	1
Project Name	Residence 2625 Broadway - Port Bolivar			Report Number	220801-24366
Contractor	Craig McClelland			Report Date	8/2/2022
Bill To	Craig McClelland	Contract No		PO No	COD
Job No		File No		GFS No	
Supplier					

On August 1, 2022, a Coastal Testing representative was present at the above referenced project, as scheduled to perform nuclear testing at 2625 Broadway. The technician performed four (4) compaction tests.

charges: 8 Hours Technician + 2 1/2 Hours Technician Overtime + 4 Density Test + 1 Vehicle Charge

Typed by: RR

Technician	Thomas Peagues	Test Date	8/1/2022
Lab Departure Time	8:15 AM	Project Arrival Time	10:15 AM
Lab Return Time	7:15 PM	Project Departure Time	5:15 PM
Standby Time		Lunch	1/2 Hour
Straight Hours	8 Hours	Overtime Hours	2 1/2 Hrs

Note: If applicable, concrete tests will come separately.

Respectfully Submitted:

Coastal Testing Laboratories, Inc.

D08

Revised 02/24/2016

Revised by Monique Connor

Revision approved by Joe Gallardo

The above test results relate only to items actually tested.

This report shall not be reproduced except in full without the approval of this laboratory.



COASTAL TESTING LABORATORIES, INC.

1217/1221 GEORGIA AVE. • 713-477-0121 • FAX 713-477-2277 • P.O. BOX 148 • DEER PARK, TEXAS 77536

RESULTS OF NUCLEAR DENSITY TESTS

Project Number 22-618 Service Date 8/1/2022

Project Name Residence 2625 Broadway - Port Bolivar Page 1

Location 2625 Braodway House Pad Fill Report Number 220801-24366

Contractor Craig McClelland Report Date 8/2/2022

Bill To Craig McClelland Contract No PO No COD

Job No File No GFS No

Test Date 8/1/2022

Material Type Brown Sandy Clay

ASTM D-6938-06

Method A

Method B

Compaction Required: 95%

Optimum Moisture 15.3

Maximum Dry Density 109.2

Moisture Requirement N/A

	Location	Lift	Probe Depth	Wet Density PCF	Moisture Content Percent	Dry Density PCF	Percent Maximum Density	Pass or Fail
1	5' S, 5' W, Northeast	1st	12"	120.4	11.5	108.0	98.9	Pass
2	5' N, 5' W, Southeast	1st	12"	119.8	12.0	107.0	98.0	Pass
3	5' S, 5' E, Northwest	1st	12"	119.3	12.7	105.9	96.9	Pass
4	5' N, 5' E, Southwest	1st	12"	119.6	12.9	105.9	97.0	Pass

Sample/Testing Technician Thomas Peagues

Standard Count: _____

Gauge Humboldt Serial # 7962

Density Std 3702

Moisture Std 412

Charges 4 Density Test (SEE DAILY REPORT)

Respectfully Submitted:

Typed by: RR END OF REPORT

CTL# 007

Coastal Testing Laboratories, Inc.

Revised 02/26/2016

The above test results relate only to items actually tested.

Revised by Monique Connor

This report shall not be reproduced except in full without the approval of this laboratory

Revision approved by Joe Gallardo



COASTAL TESTING LABORATORIES, INC.

1217/1221 GEORGIA AVE. • 713-477-0121 • FAX 713-477-2277 • P.O. BOX 148 • DEER PARK, TEXAS 77536

DAILY ACTIVITY REPORT

Project Number 22-618 Service Date 8/3/2022 Page 1
Project Name Residence 2625 Broadway - Port Bolivar Report Number 220803-24442
Contractor Craig McClelland Report Date 8/4/2022
Bill To Craig McClelland Contract No PO No COD
Job No File No GFS No
Supplier

On August 3, 2022, a Coastal Testing representative was present at the above referenced project, as scheduled to perform nuclear testing at 2625 Broadway. The technician performed four (4) compaction tests.

Charges: 5 1/4 Hours Technician + 4 Density Test + 1 Vehicle Charge

Typed by: RR

Technician	Thomas Peagues	Test Date	8/3/2022
Lab Departure Time	7:30 AM	Project Arrival Time	9:00 AM
Lab Return Time	12:45 PM	Project Departure Time	11:15 AM
Standby Time		Lunch	N/A
Straight Hours	5 1/4 Hours	Overtime Hours	

Note: If applicable, concrete tests will come separately.

Respectfully Submitted:


Coastal Testing Laboratories, Inc.

D08

Revised 02/24/2016

Revised by Monique Connor

Revision approved by Joe Gallardo

The above test results relate only to items actually tested.

This report shall not be reproduced except in full without the approval of this laboratory.



COASTAL TESTING LABORATORIES, INC.

1217/1221 GEORGIA AVE. • 713-477-0121 • FAX 713-477-2277 • P.O. BOX 148 • DEER PARK, TEXAS 77536

RESULTS OF NUCLEAR DENSITY TESTS

Project Number 22-618 Service Date 8/3/2022 Page 1

Project Name Residence 2625 Broadway - Port Bolivar Report Number 220803-24442

Location 2625 Braodway Report Date 8/4/2022

Contractor Craig McClelland PO No COD

Bill To Craig McClelland Contract No GFS No

Job No File No Test Date 8/3/2022

Material Type Brown Sandy Clay

ASTM D-6938-06 Method A Method B Compaction Required: 95%

Optimum Moisture 15.3 Maximum Dry Density 109.7 Moisture Requirement N/A

	Location	Lift	Probe Depth	Wet Density PCF	Moisture Content Percent	Dry Density PCF	Percent Maximum Density	Pass or Fail
1	5' S, 5' W, Northeast	2nd	6"	120.9	16.0	104.2	95.0	Pass
2	5' N, 5' W, Southeast	2nd	6"	120.3	14.9	104.7	95.4	Pass
3	5' S, 5' E, Northwest	2nd	6"	120.3	15.3	104.3	95.1	Pass
4	5' N, 5' E, Southwest	2nd	6"	119.9	14.2	105.0	95.7	Pass


Sample/Testing Technician Thomas Peagues Standard Count: _____

Gauge Humboldt Serial # 7962 Density Std 3742 Moisture Std 408

Charges 4 Density Test (SEE DAILY REPORT)

Typed by: RR END OF REPORT

Respectfully Submitted:



Coastal Testing Laboratories, Inc.

CTL# D07

Revised 02/26/2016

Revised by Monique Connor

Revision approved by Joe Gallardo

The above test results relate only to items actually tested.

This report shall not be reproduced except in full without the approval of this laboratory



COASTAL TESTING LABORATORIES, INC.

1217/1221 GEORGIA AVE. • 713-477-0121 • FAX 713-477-2277 • P.O. BOX 148 • DEER PARK, TEXAS 77536

DAILY ACTIVITY REPORT

Project Number 22-618 Service Date 8/9/2022 Page 1
Project Name Residence 2625 Broadway - Port Bolivar Report Number 220809-24578
Contractor Craig McClelland Report Date 8/10/2022
Bill To Craig McClelland Contract No PO No COD
Job No File No GFS No
Supplier

On August 9, 2022, a Coastal Testing representative was present at the above referenced project, as scheduled to perform nuclear testing at 2625 Broadway. The technician performed four (4) compaction tests.


charges: 4 Hours Technician + 4 Density Test + 1 Vehicle Charge

Typed by: RR

Technician	Thomas Peagues	Test Date	8/9/2022
Lab Departure Time	11:00 AM	Project Arrival Time	12:30 PM
Lab Return Time	3:00 PM	Project Departure Time	1:30 PM
Standby Time		Lunch	N/A
Straight Hours	4 Hours	Overtime Hours	

Note: If applicable, concrete tests will come separately.

Respectfully Submitted:


Coastal Testing Laboratories, Inc.

D08

Revised 02/24/2016

Revised by Monique Connor

Revision approved by Joe Gallardo

The above test results relate only to items actually tested.

This report shall not be reproduced except in full without the approval of this laboratory.



COASTAL TESTING LABORATORIES, INC.

1217/1221 GEORGIA AVE. • 713-477-0121 • FAX 713-477-2277 • P.O. BOX 148 • DEER PARK, TEXAS 77536

RESULTS OF NUCLEAR DENSITY TESTS

Project Number 22-618 Service Date 8/9/2022 Page 1
 Project Name Residence 2625 Broadway - Port Bolivar Report Number 220809-24578
 Location 2625 Broadway Report Date 8/10/2022
 Contractor Craig McClelland PO No COD
 Bill To Craig McClelland Contract No GFS No
 Job No File No Test Date 8/9/2022

Material Type Brown Sandy Clay

ASTM D-6938-06 Method A Method B

Compaction Required: 95%

Optimum Moisture 15.3 Maximum Dry Density 109.2

Moisture Requirement N/A

	Location	Lift	Probe Depth	Wet Density PCF	Moisture Content Percent	Dry Density PCF	Percent Maximum Density	Pass or Fail
1	5' S, 5' W, Northeast	3rd	6"	119.9	15.5	103.8	95.1	Pass
2	5' N, 5' W, Southeast	3rd	6"	119.8	14.9	104.3	95.5	Pass
3	5' S, 5' E, Northwest	3rd	6"	119.8	14.4	104.7	95.9	Pass
4	5' N, 5' E, Southwest	3rd	6"	120.4	13.5	106.1	97.1	Pass

Sample/Testing Technician Thomas Peagues Standard Count:
 Gauge Humboldt Serial # 7962 Density Std 3545 Moisture Std 415

Charges 4 Density Test (SEE DAILY REPORT)
 Typed by: RR END OF REPORT

Respectfully Submitted:

 Coastal Testing Laboratories, Inc.

CTL# D07
 Revised 02/26/2016
 Revised by Monique Connor
 Revision approved by Joe Gallardo

The above test results relate only to items actually tested.
 This report shall not be reproduced except in full without the approval of this laboratory



COASTAL TESTING LABORATORIES, INC.

1217/1221 GEORGIA AVE. • 713-477-0121 • FAX 713-477-2277 • P.O. BOX 148 • DEER PARK, TEXAS 77536

DAILY ACTIVITY REPORT

Project Number 22-618 Service Date 8/10/2022 Page 1
Project Name Residence 2625 Broadway - Port Bolivar Report Number 220810-24616
Contractor Craig McClelland Report Date 8/11/2022
Bill To Craig McClelland Contract No PO No COD
Job No File No GFS No
Supplier

On August 10, 2022, a Coastal Testing representative was present at the above referenced project, as scheduled to perform nuclear testing at 2625 Broadway. The technician performed eight (8) compaction tests.

charges: 4 3/4 Hours Technician + 8 Density Test + 1 Vehicle Charge

Typed by: RR

Technician	Thomas Peagues	Test Date	8/10/2022
Lab Departure Time	12:00 PM	Project Arrival Time	1:15 PM
Lab Return Time	4:45 PM	Project Departure Time	3:30 PM
Standby Time		Lunch	N/A
Straight Hours	4 3/4 Hours	Overtime Hours	

Note: If applicable, concrete tests will come separately.

Respectfully Submitted:


Coastal Testing Laboratories, Inc.

D08

Revised 02/24/2016

Revised by Monique Connor

Revision approved by Joe Gallardo

The above test results relate only to items actually tested.

This report shall not be reproduced except in full without the approval of this laboratory.



COASTAL TESTING LABORATORIES, INC.

1217/1221 GEORGIA AVE. • 713-477-0121 • FAX 713-477-2277 • P.O. BOX 148 • DEER PARK, TEXAS 77536

RESULTS OF NUCLEAR DENSITY TESTS

Project Number 22-618 Service Date 8/10/2022

Project Name Residence 2625 Broadway - Port Bolivar Page 1

Location 2625 Braodway Report Number 220810-24616

Contractor Craig McClelland Report Date 8/11/2022

Bill To Craig McClelland Contract No PO No COD

Job No File No GFS No

Test Date 8/10/2022

Material Type Brown Sandy Clay

ASTM D-6938-06 Method A Method B

Optimum Moisture 15.3 Maximum Dry Density 109.2

Compaction Required: 95%

Moisture Requirement N/A

	Location	Lift	Probe Depth	Wet Density PCF	Moisture Content Percent	Dry Density PCF	Percent Maximum Density	Pass or Fail
1	5' S, 5' W, Northeast	4th	12"	118.4	14.0	103.9	95.1	Pass
2	5' N, 5' W, Southeast	4th	12"	118.0	13.7	103.8	95.0	Pass
3	5' S, 5' E, Northwest	4th	12"	118.5	13.3	104.6	95.8	Pass
4	5' N, 5' E, Southwest	4th	12"	119.1	14.2	104.3	95.5	Pass
5	5' S, 5' W, Northeast	5th	12"	119.6	13.5	105.4	96.5	Pass
6	5' N, 5' W, Southeast	5th	12"	118.7	14.1	104.0	95.3	Pass
7	5' S, 5' E, Northwest	5th	12"	119.5	13.9	104.9	96.1	Pass
8	5' N, 5' E, Southwest	5th	12"	119.4	12.8	105.9	96.9	Pass

Sample/Testing Technician Thomas Peagues Standard Count: _____

Gauge Humboldt Serial # 7962 Density Std 3862 Moisture Std 402

Charges 8 Density Test (SEE DAILY REPORT)

Typed by: RR END OF REPORT

Respectfully Submitted:

Tom Peagues

Coastal Testing Laboratories, Inc.

CTL# D07

Revised 02/26/2016

Revised by Monique Connor

Revision approved by Joe Gallardo

The above test results relate only to items actually tested.

This report shall not be reproduced except in full without the approval of this laboratory



COASTAL TESTING LABORATORIES, INC.

1217/1221 GEORGIA AVE. • 713-477-0121 • FAX 713-477-2277 • P.O. BOX 148 • DEER PARK, TEXAS 77536

DAILY ACTIVITY REPORT

Project Number	22-618	Service Date	8/15/2022	Page	1
Project Name	Residence 2625 Broadway - Port Bolivar			Report Number	220815-24694
Contractor	Craig McClelland			Report Date	8/16/2022
Bill To	Craig McClelland	Contract No		PO No	COD
Job No		File No		GFS No	
Supplier					

On August 15, 2022, a Coastal Testing representative was present at the above referenced project, as scheduled to perform nuclear testing at 2625 Broadway. The technician performed eight (8) compaction tests.

charges: 4 1/2 Hours Technician + 8 Density Test + 1 Vehicle Charge

Typed By: Rr

Technician	Thomas Peagues	Test Date	8/15/2022
Lab Departure Time	8:15 AM	Project Arrival Time	9:45 AM
Lab Return Time	12:45 PM	Project Departure Time	11:15 AM
Standby Time		Lunch	N/A
Straight Hours	4 1/2 Hours	Overtime Hours	

Note: If applicable, concrete tests will come separately.

Respectfully Submitted:


 Coastal Testing Laboratories, Inc.



COASTAL TESTING LABORATORIES, INC.

1217/1221 GEORGIA AVE. • 713-477-0121 • FAX 713-477-2277 • P.O. BOX 148 • DEER PARK, TEXAS 77536

RESULTS OF NUCLEAR DENSITY TESTS

Project Number 22-618 Service Date 8/15/2022 Page 1

Project Name Residence 2625 Broadway - Port Bolivar Report Number 220815-24694

Location 2625 Braodway Report Date 8/16/2022

Contractor Craig McClelland Contract No PO No COD

Bill To Craig McClelland Contract No GFS No

Job No File No Test Date 8/15/2022

Material Type Brown Sandy Clay

ASTM D-6938-06

Method A Method B

Compaction Required: 95%

Optimum Moisture 15.3

Maximum Dry Density 109.2

Moisture Requirement N/A


Location	Lift	Probe Depth	Wet Density PCF	Moisture Content Percent	Dry Density PCF	Percent Maximum Density	Pass or Fail
1 5' S, 5' W, Northeast	6th	6"	121.4	17.0	103.8	95.0	Pass
2 5' N, 5' W, Southeast	6th	6"	121.8	16.8	104.3	95.5	Pass
3 5' S, 5' E, Northwest	6th	6"	122.0	17.2	104.1	95.3	Pass
4 5' N, 5' E, Southwest	6th	6"	121.7	16.4	104.6	95.7	Pass
5 5' S, 5' W, Northeast	7th	6"	122.0	15.8	105.4	96.5	Pass
6 5' N, 5' W, Southeast	7th	6"	121.9	16.4	104.7	95.9	Pass
7 5' S, 5' E, Northwest	7th	6"	122.0	15.0	106.1	97.1	Pass
8 5' N, 5' E, Southwest	7th	6"	122.3	15.5	105.9	97.0	Pass

Sample/Testing Technician Thomas Peagues Standard Count: _____

Gauge Humboldt Serial # 7962 Density Std 3358 Moisture Std 470

Charges 8 Density Test (SEE DAILY REPORT)

Typed by: RR END OF REPORT

Respectfully Submitted:

 Coastal Testing Laboratories, Inc.

CTL# D07
 Revised 02/26/2016
 Revised by Monique Connor
 Revision approved by Joe Gallardo

The above test results relate only to items actually tested.
 This report shall not be reproduced except in full without the approval of this laboratory



COASTAL TESTING LABORATORIES, INC.

1217/1221 GEORGIA AVE. • 713-477-0121 • FAX 713-477-2277 • P.O. BOX 148 • DEER PARK, TEXAS 77536

RESULTS OF NUCLEAR DENSITY TESTS

Project Number 22-618	Service Date 9/15/2022	Page 1
Project Name Residence 2625 Broadway - Port Bolivar		Report Number 220915-25336
Location 2625 Braodway		Report Date 9/16/2022
Contractor Craig McClelland		PO No COD
Bill To Craig McClelland	Contract No	GFS No
Job No	File No	Test Date 9/15/2022

Material Type Brown Sandy Clay

ASTM D-6938-06

Method A

Method B

Compaction Required: 95%

Optimum Moisture 15.3

Maximum Dry Density 109.2

Moisture Requirement N/A

	Location	Lift	Probe Depth	Wet Density PCF	Moisture Content Percent	Dry Density PCF	Percent Maximum Density	Pass or Fail
1	10' S, 10' E, Northwest	1st & Final	6"	119.9	14.3	104.9	96.1	Pass
2	10' S, 10' W, Northeast	1st & Final	6"	121.4	13.9	106.6	97.6	Pass
3	10' N, 10' W, Southeast	1st & Final	6"	119.5	13.5	105.3	96.4	Pass
4	10' N, 10' E, Southwest	1st & Final	6"	120.6	15.5	104.4	95.6	Pass

Sample/Testing Technician James Bruno Standard Count: _____
 Gauge Humboldt Serial # 9724 Density Std 2786 Moisture Std 385

Charges 4 Hours Technician + 4 Density Test + 1 Vehicle Charge
 Typed by: RR END OF REPORT

Respectfully Submitted:

 Coastal Testing Laboratories, Inc.

CTL# D07
 Revised 02/26/2016
 Revised by Monique Connor
 Revision approved by Joe Gallardo

The above test results relate only to items actually tested.
 This report shall not be reproduced except in full without the approval of this laboratory
